







KANSAS HIGHWAY SYSTEM District 4

2013 Performance Levels

-  Level One: 91.2% 1,613 MI
-  Level Two: 8.6% 152 MI
-  Level Three: 0.2% 4 MI



(Note: Mapped data includes HPMS segments on State network excluded from summary totals)

Year of Projects

-  2013 Locations
-  2014 Locations
-  2015 Locations

- 8 ChipSeal
- 11 Overlay .75"
- 12 Overlay 1.5"
- 14 Overlay 4"
- 15 SR 1", OL 1"
- 42 FD PCCP Patching
- 200 New Const (IFD=4)
- 201 New Const (IFD=3)
- 221 Rout & CrackSeal
- 300 Overlay 1"
- 347 CM 2", OL 2"
- 348 UBAS-Novachip
- 359 CM 4", OL 6"
- 375 CM 1.5", OL 1.5"
- 380 CM 5", OL 1"
- 385 CM 1", OL 1.5"
- 428 CM 1", OL 1"

prepared by
Kansas Department of Transportation
Bureau of Construction and Materials
based on database snapshot from
November 1, 2013

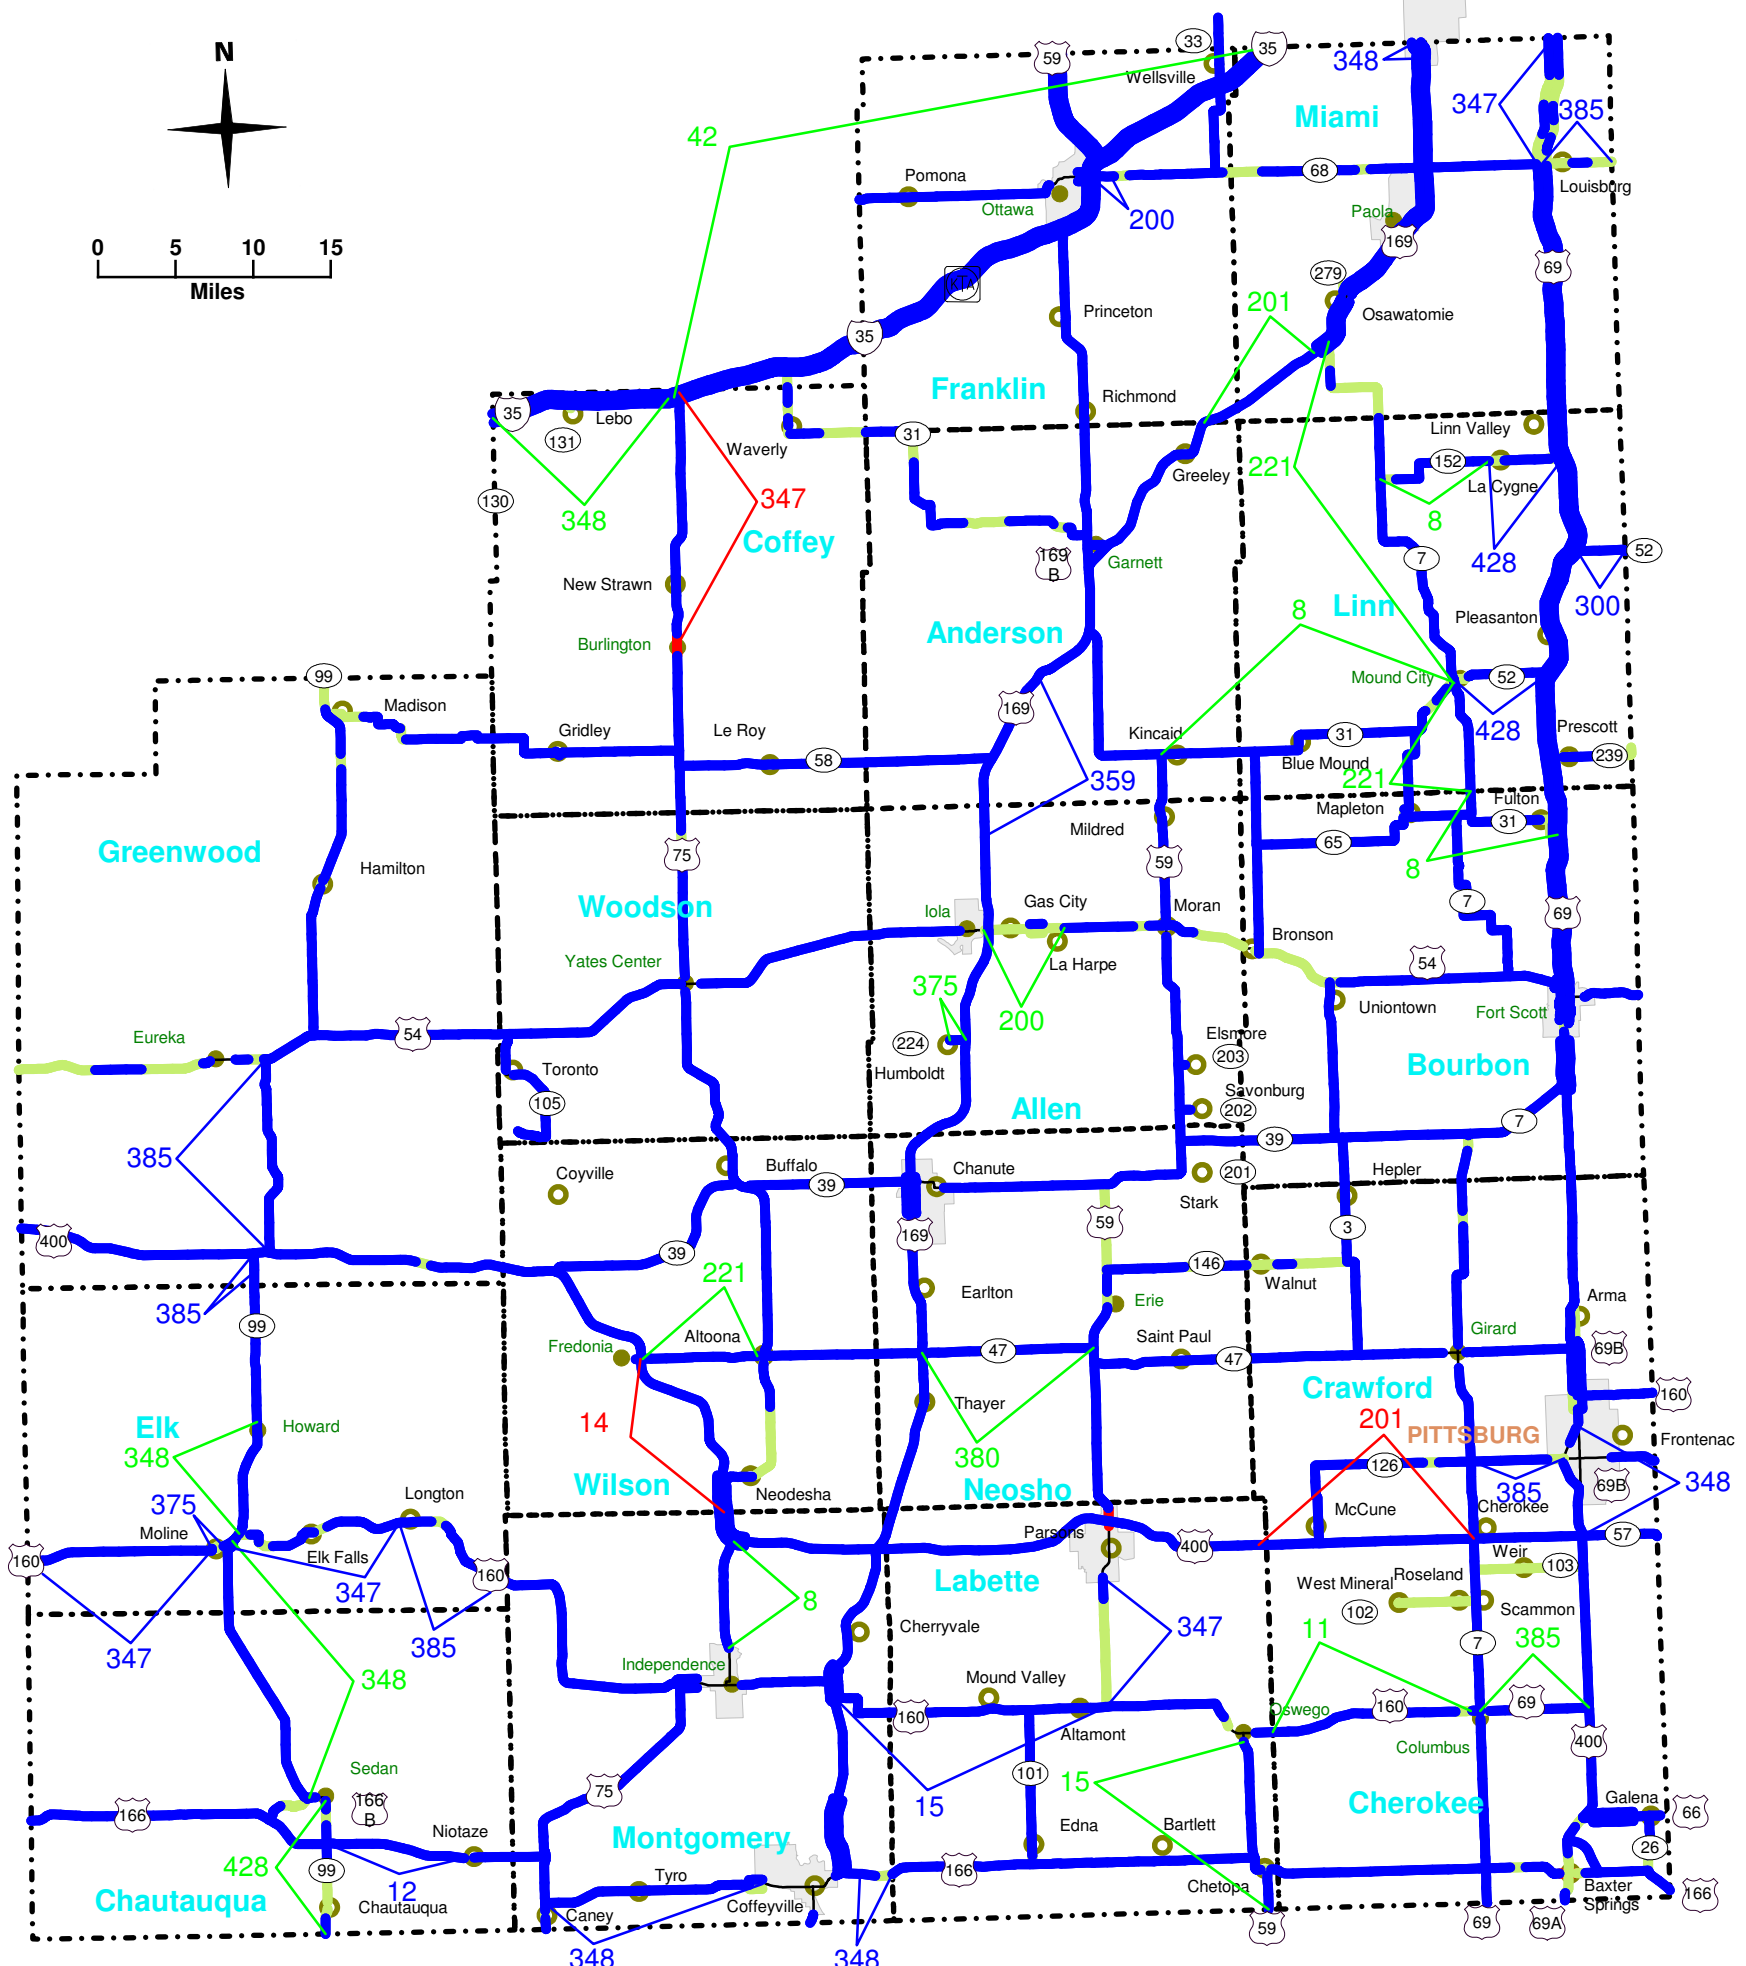

KDOT makes no warranties, guarantees, or representations for accuracy of this information and assumes no liability or responsibility for any errors or omissions.
